


ARCHITECT'S SITE OBSERVATION REPORT

No. 15



2016-04-13

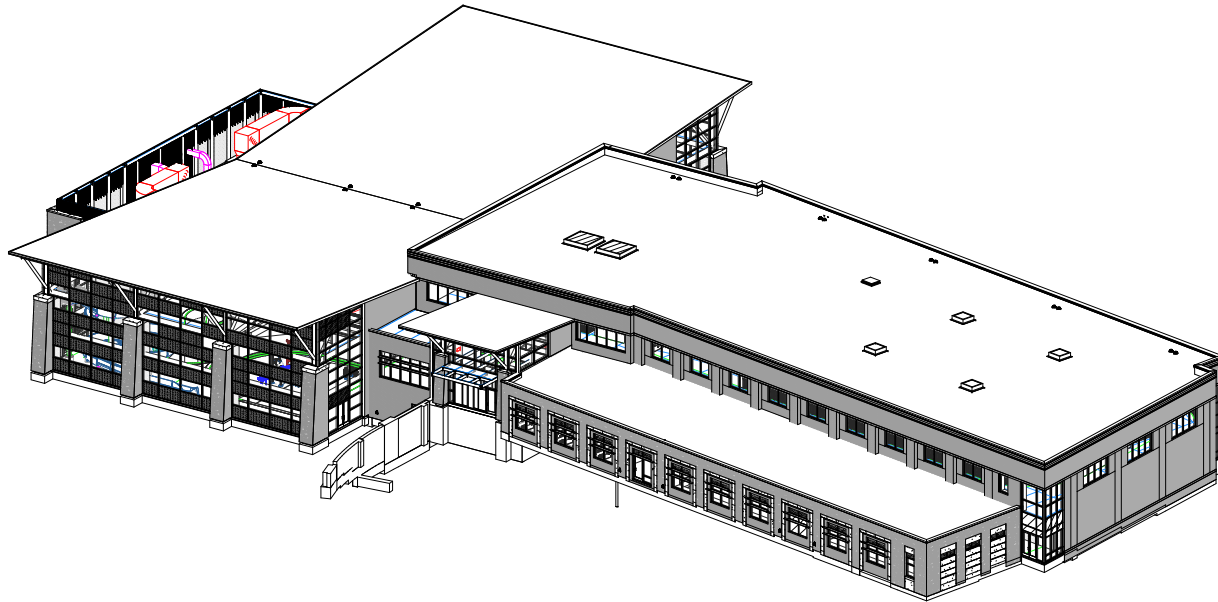

McKINNEY AQUATIC & FITNESS CENTER

PROJECT NUMBER: 21406
OWNER: CITY OF McKINNEY

START DATE OF CONSTRUCTION: AUGUST 10, 2015
SUBSTANTIAL COMPLETION DATE: NOVEMBER 22, 2016

TIME: 9:00AM

WEATHER: Rainy/Wet/Muddy

LOCATION: ONSITE

REPORT BY BSW: MICHAEL L. WOODS



WORK IN PROGRESS:

Trusses at Natatorium are nearly complete and misc steel is being installed. Indoor CMU is ongoing. Overhead MEP is taking place in Area A and B. MEP in wall rough-in's are taking place and are ongoing. Plumbing carriers are being set. Door frames are being set as CMU moves along. Fire lane pours are still ongoing (approx 3 left). Metal studs, sheathing, weather barrier and insulation is being installed. Damproofing at the Natatorium is being installed and fluid applied Air and Water barrier is being installed at other locations. Waterproofing and flashing is being installed. The stone is being installed at the West end of Area A and brick has begun installation. Roofing is nearly complete at Area B and will move onto Area A once the deck is installed. Pool Piping and Pool Mech Equipment is being installed.

The Outdoor Leisure pool shell is nearly complete with exception of the beach entries. Bath house CMU is installed.

















