

# TUPPS Brewery Expansion Project – June 2022 Construction Update


SpawGlass [SG] mobilized on site February 28. They continue buyout of subcontractors/vendors for the project.

The Current Schedule indicates that the project (in full) will be substantially complete November 2, 2022.

Below is a high-level recap of work progress and photos.

## May 31 – June 4

Sanitary Sewer for Brewery and prefab work for piping, building forms for grade beams at Brewery, backfill and compaction at Kitchen area expansion, pumping rainwater out of grade beam ditches.

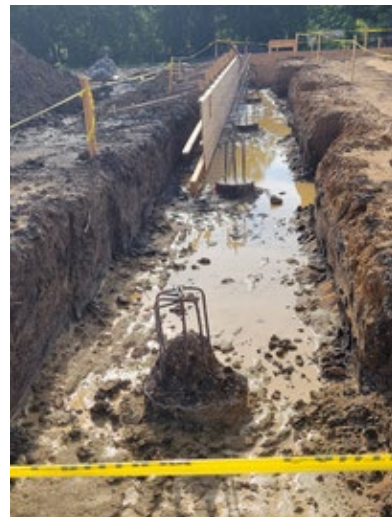

**June 6 – June 11**

Underground plumbing installation in progress, forming grade beams, setting rebar at Brewery Bldg, salvage of wood from middle building, demo of trees and concrete pad of center building,





**June 13 – June 18**

Brewery building- back filling plumbing trenches, pouring grade beams, tree trimming for ONCOR lines, placing plumbing lines at Brewery



**June 20 – June 25**

Brewery plumbing pipes, electrical conduit, storm water pipe, pouring grade beams







**June 27 – July 1**

Strip grade beam forms, digging and forming for elevator base, install conduit under grade beams at Brewery, backfill at storm water piping,







**TUPPS Brewery & Entertainment Destination  
Concrete Pour 7/21/22**

