


ARCHITECT'S SITE OBSERVATION REPORT

No. 3



2015-10-01

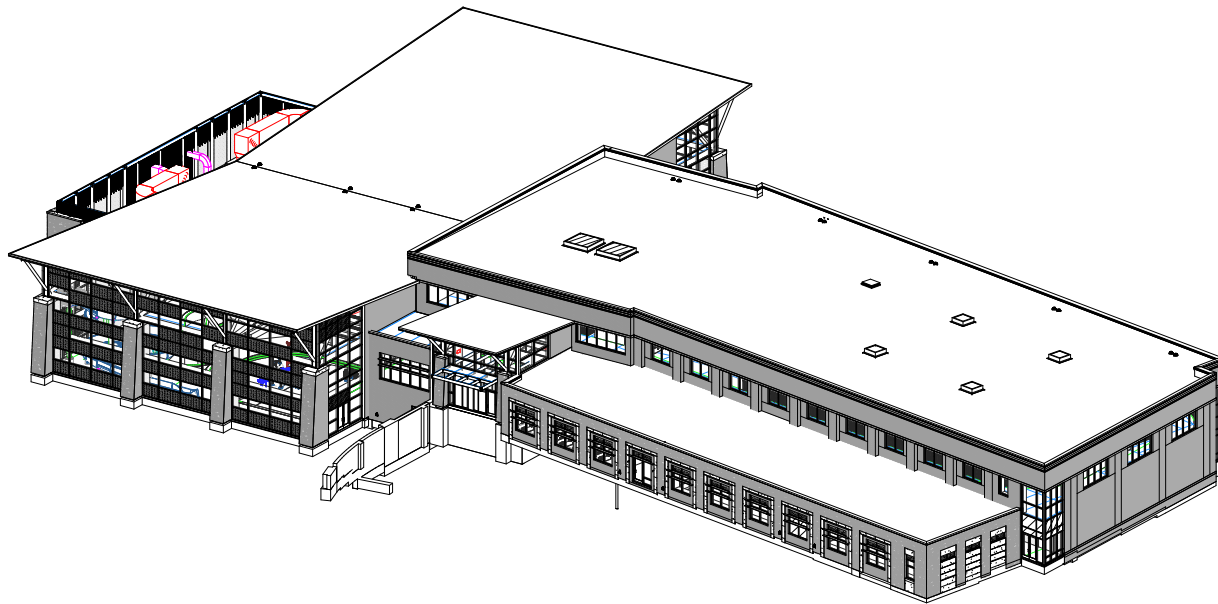

McKINNEY AQUATIC & FITNESS CENTER

PROJECT NUMBER: 21406
OWNER: CITY OF McKINNEY

START DATE OF CONSTRUCTION: AUGUST 10, 2015
SUBSTANTIAL COMPLETION DATE: NOVEMBER 1, 2016

TIME: 9:00AM

WEATHER: SUNNY

LOCATION: ONSITE

REPORT BY BSW: MICHAEL L. WOODS



WORK IN PROGRESS:

Cut and fill operations are progressing at this time. Most of the excess soil is being place on the South of the property. Site utilities are being installed (Storm, Water, and Sewer). The Competition pool is completely excavated and the under pool drainage system will be installed soon. The Leisure pool is being excavated at this time also, but is not complete yet. Piers are complete and the grade beams on the West side of Area A (Pool Mech Pit Area) are being formed, reinforced and poured. Underground plumbing is being installed at Area A. Fire Lanes are in the process of being prepped however cannot be installed until site utilities are 100% complete and inspected.











