


ARCHITECT'S SITE OBSERVATION REPORT

No. 9



2016-01-06

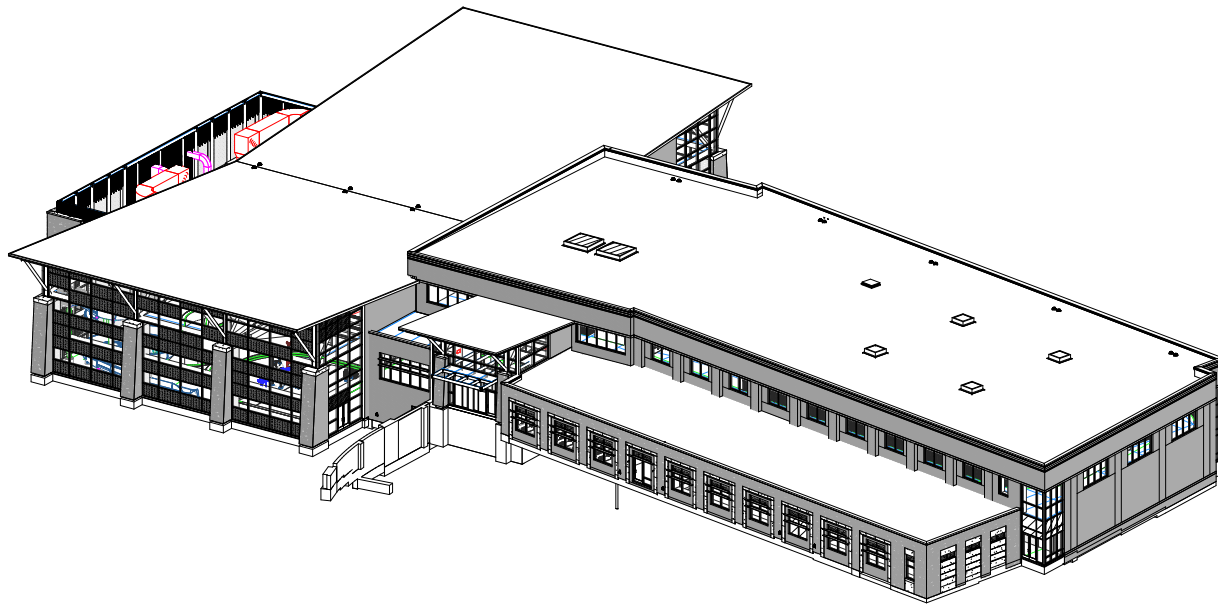

McKINNEY AQUATIC & FITNESS CENTER

PROJECT NUMBER: 21406
OWNER: CITY OF McKINNEY

START DATE OF CONSTRUCTION: AUGUST 10, 2015
SUBSTANTIAL COMPLETION DATE: NOVEMBER 1, 2016

TIME: 9:00AM

WEATHER: SUNNY

LOCATION: ONSITE

REPORT BY BSW: MICHAEL L. WOODS



WORK IN PROGRESS:

The majority of the Fire Lane is complete and enough has been installed so the Contractor can start vertical construction. The remaining Fire Lanes are still ongoing and should be complete soon. Pool Piping for the Indoor Leisure and Indoor Competition Pool is being installed and the wall will be backfilled soon. The Indoor Leisure pool has been poured. Level 1 Area B has been poured. Structural Steel will start soon and Level 2 Area B will be decked and poured in approx 2 weeks. CMU at the Pool Mech Area is being installed and will continue from the West to the East. MEP rough-ins are ongoing.













