


# ARCHITECT'S SITE OBSERVATION REPORT

No. 13



2016-03-02

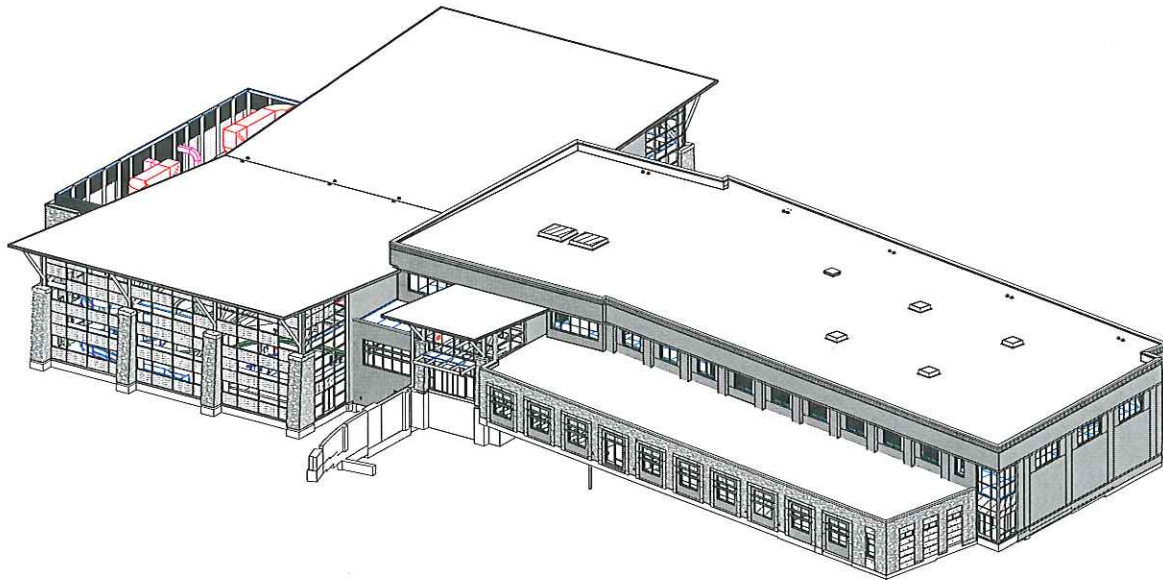

## McKINNEY AQUATIC & FITNESS CENTER

PROJECT NUMBER: 21406  
OWNER: CITY OF McKINNEY

START DATE OF CONSTRUCTION: AUGUST 10, 2015  
SUBSTANTIAL COMPLETION DATE: NOVEMBER 22, 2016

TIME: 9:00AM

WEATHER: SUNNY

LOCATION: ONSITE

REPORT BY BSW: MICHAEL L. WOODS



**WORK IN PROGRESS:**

Area B Structural Steel at Natatorium is being installed. Stairs are being installed. The Outdoor Leisure pool is being F/R/P. Pool bottom will be poured first, then the walls will be shotcreted. The Indoor Leisure pool deck has been poured and is protected with plywood. Indoor CMU is ongoing. Bath house CMU is up. MEP in wall rough-in are taking place and are ongoing. Plumbing carriers are being set. Overhead MEP is taking place in Area B (lower level) and in parts of Area A also. Door frames are being set as CMU moves along. Fire lane pours are still ongoing (approx 3 left). Metal Studs, Sheathing, Weather barrier and insulation is being installed. Damproofing at the Natatorium is being installed. The stone will arrive soon and will start installation. The new brick is scheduled to arrive around the end of March.





















































