



ARCHITECT'S SITE OBSERVATION REPORT

No. 11



2016-02-03

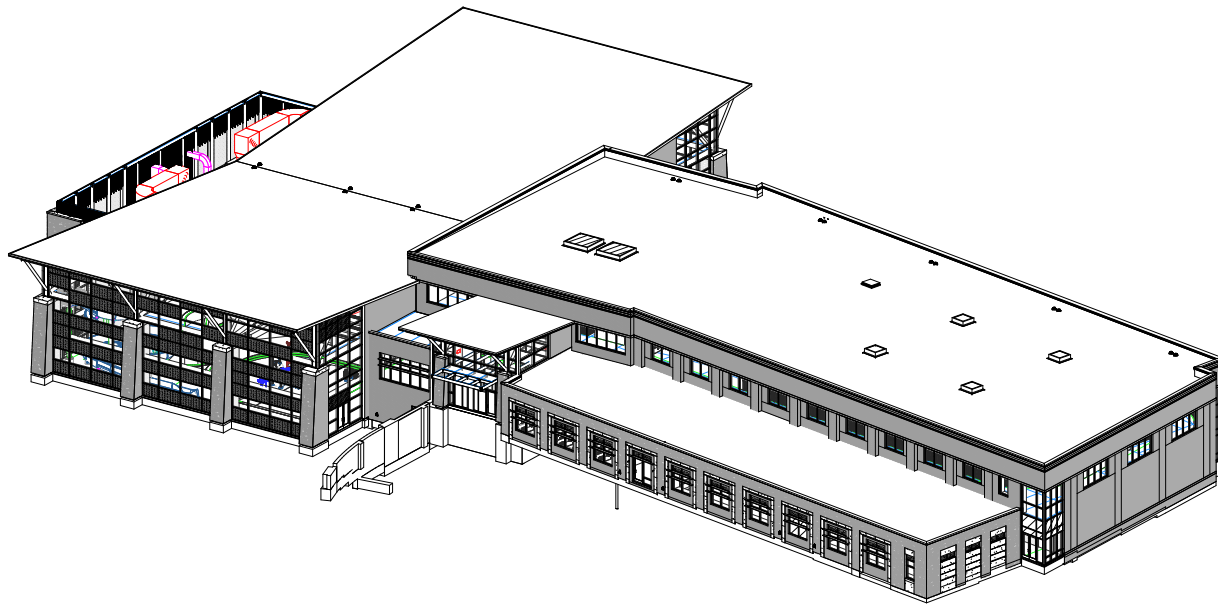

McKINNEY AQUATIC & FITNESS CENTER

PROJECT NUMBER: 21406
OWNER: CITY OF McKINNEY

START DATE OF CONSTRUCTION: AUGUST 10, 2015
SUBSTANTIAL COMPLETION DATE: NOVEMBER 22, 2016

TIME: 9:00AM

WEATHER: SUNNY


LOCATION: ONSITE

REPORT BY BSW: MICHAEL L. WOODS



WORK IN PROGRESS:

Structural steel and joists/deck at Area B are being installed. Level 2 Area A has been poured and re-shores are installed. The Outdoor Leisure pool is being F/R/P. The Comp pool deck has been poured and the Leisure pool deck is being fine graded. The trench drain elevations are currently being coordinated. The leisure pool deck will be poured on Friday. CMU will be moving toward 5 line @ AB-AC line and into the Party Room Area. Door frames are being set as CMU move along. 4 Additional 4" conduits for utilities will be installed (per City Request) before the slab at the service yard is poured. Paving areas will continue to be poured. Fire lane pours are still ongoing (approx 3 left). Metal Studs, Sheathing, Weather barrier and insulation will be installed soon.

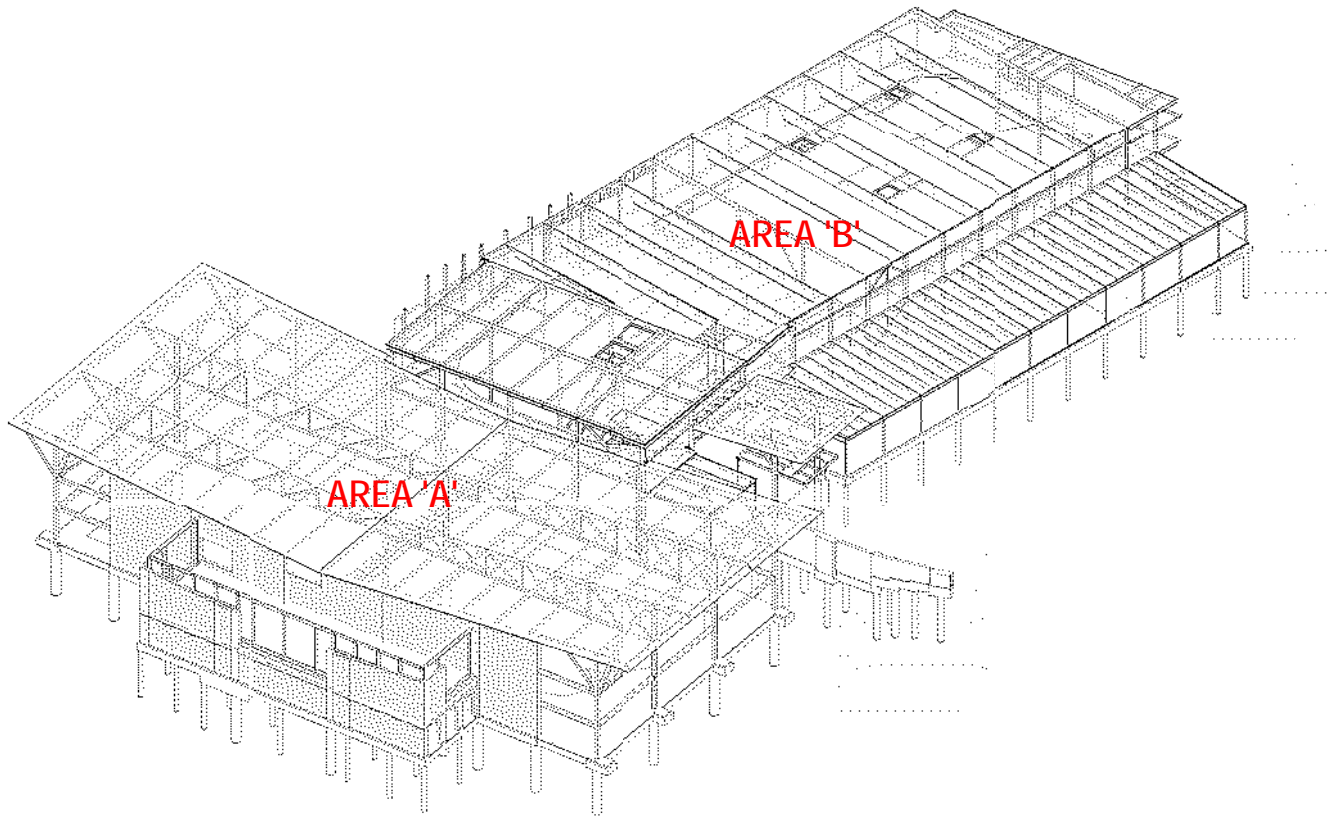



Manhattan
Building excellence.



Aquatic & Fitness Center

Print #160201798

Date: 02/01/16

Lat/Lon: 33.172764 -96.714439

Order No. 59827



Aerial Photography, Inc. 954-568-0484





