



ARCHITECT'S SITE OBSERVATION REPORT

No. 1



2015-09-02

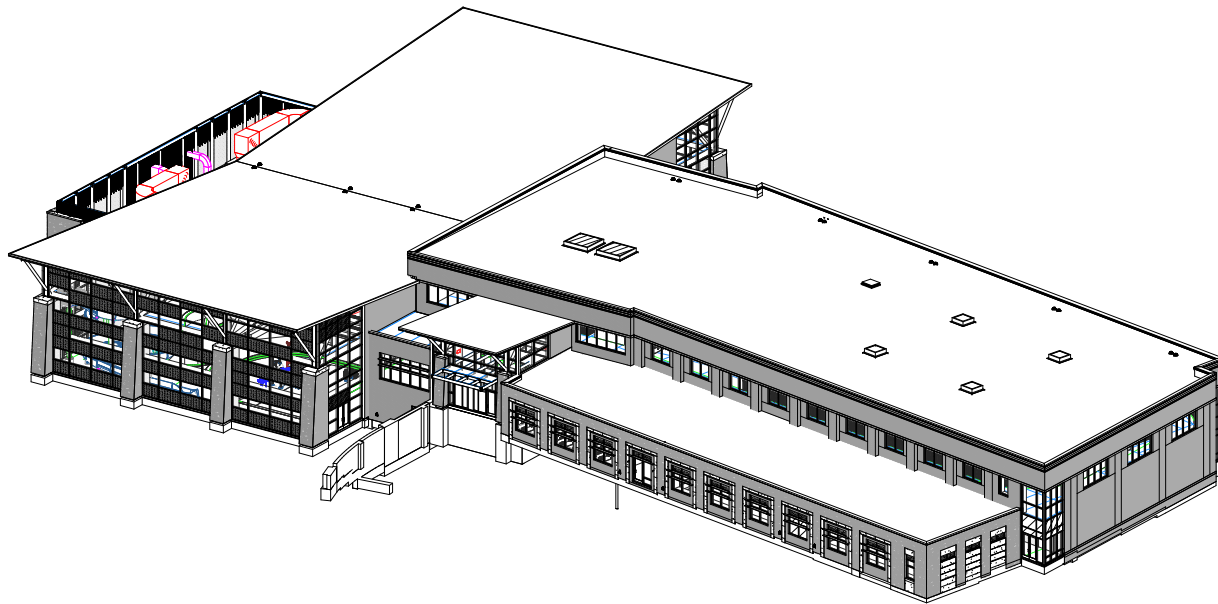

McKINNEY AQUATIC & FITNESS CENTER

PROJECT NUMBER: 21406
OWNER: CITY OF McKINNEY

START DATE OF CONSTRUCTION: AUGUST 10, 2015
SUBSTANTIAL COMPLETION DATE: NOVEMBER 1, 2016

TIME: 9:00AM

WEATHER: SUNNY

LOCATION: ONSITE

REPORT BY BSW: MICHAEL L. WOODS



WORK IN PROGRESS:

The Contractor has completely mobilized at this time and a perimeter fence has been installed around the site.

Cut and fill operations are progressing at this time. Most of the excess soil is being placed on the South of the property. Moisture conditioning under the building pad is taking place. Some select fill is being placed and compacted. Site utilities are expected to begin soon.





